

ASSIGNMENT

FAKE CLIENT PROJECT SIMULATION

Requirements → Planning → Execution → Delivery → Revisions → Pricing → Final Acceptance

Domain: AI Automation / Digital Business Solution

Project Type: Professional Client Project

Perspective: Freelancer / AI Consultant / Automation Specialist

Objective: Ek realistic client project ko end-to-end solve karna

TABLE OF CONTENTS

1. Executive Summary
2. Assignment Introduction
3. Purpose of the Assignment
4. Fake Client Profile
5. Client Business Background
6. Client Problem
7. Initial Client Brief
8. Stakeholder Analysis
9. Client Expectations
10. Business Goals
11. Project Goals
12. Functional Requirements
13. Non-Functional Requirements
14. Technical Requirements
15. User Requirements
16. Business Requirements
17. Requirements Discovery Process
18. Requirement Questions
19. Requirement Prioritization
20. Scope Definition
21. In-Scope Items
22. Out-of-Scope Items
23. Assumptions

24. Dependencies
25. Constraints
26. Success Criteria
27. Deliverables
28. Project Architecture
29. Technology Stack
30. Project Workflow
31. Project Phases
32. Timeline
33. Milestones
34. Resource Planning
35. Communication Plan
36. Project Management Strategy
37. Pricing Strategy
38. Cost Estimation
39. Payment Structure
40. Proposal
41. Client Approval
42. Development Process
43. Quality Assurance
44. Testing Strategy
45. Client Demo
46. Initial Delivery
47. Client Feedback
48. Revision Management
49. Revision Rounds
50. Change Request vs Revision
51. Scope Creep
52. Change Control Process
53. Additional Pricing
54. Final Delivery
55. Client Acceptance
56. Documentation
57. Training
58. Handover
59. Post-Delivery Support
60. Risk Management
61. Security

- 62. Backup & Recovery
- 63. Performance
- 64. Maintenance
- 65. Client Satisfaction
- 66. Lessons Learned
- 67. Final Project Evaluation
- 68. Professional Best Practices
- 69. Conclusion
- 70. Final Deliverables Checklist

1. Executive Summary

This assignment presents a realistic **fake-client project simulation** in which an AI automation consultant receives a project from a fictional client and manages the project from initial requirements gathering to final delivery.

The project demonstrates three core professional skills:

- **Requirements Management**
- **Delivery Management**
- **Revision Management**
- **Professional Pricing**

However, these activities cannot be handled independently. A professional project requires interconnected processes including:

Client Discovery → Requirements → Scope → Proposal → Pricing → Agreement → Planning → Development → Testing → Review → Revisions → Delivery → Acceptance → Handover → Support

The purpose of this assignment is therefore to demonstrate how an AI professional can convert an unclear client request into a structured, measurable and deliverable solution.

2. Fake Client Profile

Client Name

Apex Digital Marketing Agency

Industry

Digital Marketing / Social Media Marketing

Location

Lahore, Pakistan

Business Size

Small-to-medium digital agency

Employees

12

Target Customers

- Small businesses
- E-commerce stores
- Personal brands
- Coaches
- Local businesses
- Startups

Current Problem

The agency manually performs social-media research, content planning and reporting.

This consumes significant employee time.

3. Client Background

Apex Digital Marketing manages social-media accounts for approximately 20 clients.

Every week, employees manually:

1. Search for trends.
2. Research competitors.
3. Identify content ideas.
4. Write captions.
5. Create content briefs.
6. Send ideas to clients.
7. Wait for approval.
8. Update spreadsheets.
9. Prepare reports.

The company wants to automate a large portion of this process.

4. Initial Client Brief

The fictional client initially says:

"We want an AI system that finds social-media trends, creates content ideas, sends them to our team for approval, and helps us publish the content automatically."

At first glance this appears simple.

However, the statement is **not sufficient as a development specification**.

It does not define:

- Which platforms?
- Which accounts?
- Which trends?
- How frequently?
- Which AI model?

- What content?
- Who approves?
- How approval happens?
- What happens after rejection?
- How many revisions?
- What counts as a revision?
- What happens when an API fails?
- What is the budget?
- What is the delivery date?
- What happens after delivery?

Therefore, the first professional task is **requirements discovery**.

5. Client Problem Statement

The client's existing workflow is:

Manual Research → Manual Idea Generation → Manual Approval → Manual Content Preparation → Manual Publishing → Manual Reporting

This creates:

- High labor cost
- Slow execution
- Human error
- Inconsistent content quality
- Delayed publishing
- Poor scalability
- Repetitive work

The desired workflow is:

Automated Research → AI Analysis → Content Generation → Human Approval → Automated Publishing → Analytics

6. Business Goals

The client wants to:

1. Reduce manual research.
2. Reduce repetitive content work.
3. Increase publishing consistency.
4. Improve response speed to trends.
5. Manage multiple clients efficiently.
6. Reduce operational cost.
7. Scale the agency without proportionally increasing staff.

8. Maintain human approval before publishing.
9. Create measurable reporting.

7. Project Goals

The project will deliver an AI-powered content workflow capable of:

- Trend discovery
- Trend analysis
- Content idea generation
- Caption generation
- Approval management
- Revision requests
- Content preparation
- Publishing workflow
- Logging
- Basic analytics

8. Requirements Discovery

Before development, the consultant conducts a requirements interview.

Questions

Business

- What business problem are we solving?
- What does success look like?
- How many users will use the system?
- How many social accounts?
- How many posts per week?

Content

- What content formats are required?
- Reels?
- Images?
- Carousels?
- Stories?
- Captions?
- Hashtags?

Automation

- What should be automated?
- What should remain human-controlled?

- What happens when AI produces poor content?

Approval

- Who approves content?
- What approval methods are required?
- WhatsApp?
- Dashboard?
- Email?

Revisions

- How many revisions are included?
- What qualifies as a revision?
- What qualifies as a new request?

Technical

- Which APIs?
- Which AI models?
- Which database?
- Which hosting environment?
- What authentication method?

Commercial

- Budget?
- Deadline?
- Payment method?
- Maintenance expectations?

9. Requirements Prioritization

Requirements are classified using **MoSCoW**.

Priority	Meaning	Example
Must Have	Essential	Trend research
Should Have	Important	Approval system
Could Have	Optional	Advanced analytics
Won't Have	Future scope	Mobile app

This prevents uncontrolled expansion.

10. Functional Requirements

The system must:

FR-01

Automatically initiate research.

FR-02

Collect trend signals.

FR-03

Normalize collected data.

FR-04

Remove duplicate trends.

FR-05

Analyze trends using AI.

FR-06

Generate content opportunities.

FR-07

Generate captions.

FR-08

Send content proposal for approval.

FR-09

Allow:

- APPROVE
- REJECT
- MODIFY

FR-10

Process modification requests.

FR-11

Generate revised content.

FR-12

Prepare approved content.

FR-13

Publish content through supported APIs.

FR-14

Store execution history.

FR-15

Record errors.

FR-16

Generate basic performance reports.

11. Non-Functional Requirements

The system should provide:

Reliability

Workflows should handle temporary failures.

Security

API credentials must not be exposed.

Scalability

Architecture should support additional clients.

Maintainability

Components should be modular.

Performance

Normal workflow execution should complete within an acceptable operational window.

Usability

Approval should require minimal user effort.

Observability

Important events should be logged.

12. Technical Requirements

Possible technology stack:

Layer	Technology
Automation	n8n
AI	LLM API
Database	PostgreSQL / Supabase
Notifications	WhatsApp Business API
Social Platform	Instagram Graph API
Backend Logic	JavaScript / Python where required
Authentication	OAuth/API credentials
Storage	Cloud object storage
Analytics	Database + dashboard
Version Control	Git

The exact implementation depends on API availability and client credentials.

13. Scope

In Scope

- Trend research workflow

- AI analysis
- Content idea generation
- Approval workflow
- Revision workflow
- Instagram publishing integration
- Database logging
- Error handling
- Basic documentation
- Client training

Out of Scope

Unless separately purchased:

- Mobile application
- Custom CRM
- Full marketing website
- Advanced BI platform
- Unlimited revisions
- Custom AI model training
- Third-party paid data subscriptions
- Full enterprise multi-tenant SaaS

This distinction is critical for preventing **scope creep**.

14. Assumptions

The project assumes:

1. Client provides required API credentials.
2. Client owns required social accounts.
3. APIs permit requested functionality.
4. Client responds to approvals within agreed time.
5. Third-party services remain operational.
6. AI-generated content requires human review.
7. Client provides brand guidelines.
8. Client provides required media assets.

15. Dependencies

The project depends on:

- Instagram API access
- WhatsApp API access

- AI provider
- Database
- n8n environment
- Client credentials
- Internet connectivity
- Third-party API availability

A dependency failure can affect delivery.

16. Constraints

Example constraints:

- Limited initial budget
- Limited development time
- API limitations
- AI usage costs
- Social platform restrictions
- Client approval delays
- Third-party service outages

17. Success Criteria

The project will be considered successful if:

- Required workflow executes correctly.
- Trend research functions.
- AI produces structured content ideas.
- Approval mechanism works.
- Revision process works.
- Approved content can reach publishing stage.
- Errors are logged.
- Client can operate the workflow.
- Documentation is delivered.
- Client formally accepts the project.


18. Deliverables

The final package contains:

1. Automation workflows
2. AI prompts
3. Database structure

4. API integrations
5. Approval workflow
6. Revision mechanism
7. Error handling
8. Testing results
9. User documentation
10. Technical documentation
11. Training session
12. Handover package

19. Project Architecture

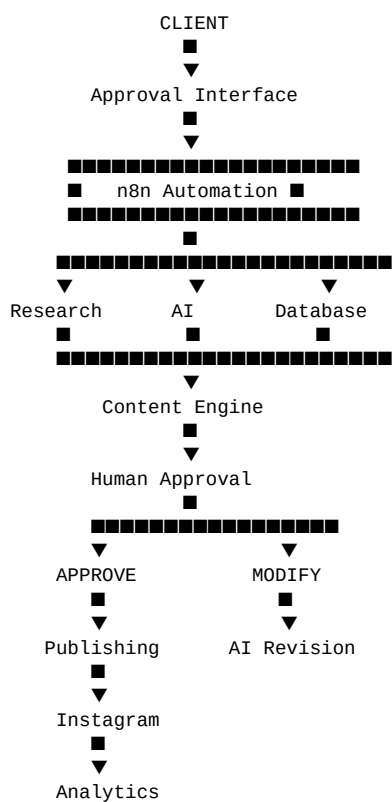

20. Project Phases

Phase 1 — Discovery

Requirements gathering.

Phase 2 — Specification

Convert requirements into technical specifications.

Phase 3 — Architecture

Design system architecture.

Phase 4 — Development

Build automation.

Phase 5 — Integration

Connect external services.

Phase 6 — Testing

Perform functional and failure testing.

Phase 7 — Client Review

Demonstrate the system.

Phase 8 — Revisions

Implement agreed revisions.

Phase 9 — Final Delivery

Deliver production version.

Phase 10 — Handover

Documentation and training.

21. Example Timeline

Phase	Duration
Discovery	1 day
Requirements	1 day
Architecture	1 day
Development	5 days
Integration	2 days
Testing	2 days
Client Review	1 day
Revisions	2 days
Final QA	1 day
Delivery	1 day
Handover	1 day

Estimated total: 18 working days

22. Milestones

M1

Requirements approved.

M2

Architecture approved.

M3

Core automation completed.

M4

Integrations completed.

M5

Testing completed.

M6

Client review completed.

M7

Revisions completed.

M8

Final acceptance.

23. Communication Plan

Communication	Frequency
Project update	Twice weekly
Technical issue	As required
Client review	At milestone
Revision discussion	After review
Final handover	End of project

A project communication channel should be agreed in advance.

24. Pricing Strategy

Professional pricing should not be based only on hours.

Pricing can consider:

Scope + Complexity + Risk + Expertise + Value + Maintenance

Example project pricing:

Component	Price
Discovery	\$100
Architecture	\$150
Automation	\$500
AI integration	\$300
API integration	\$250
Testing	\$150
Documentation	\$100
Training	\$100

Component	Price
Total	\$1,650

This is an educational example, not a market quotation.

25. Payment Structure

A professional structure could be:

40% — Upfront

Before development begins.

30% — Milestone

After functional prototype.

20% — Client Review

After integrated system demonstration.

10% — Final Delivery

After acceptance/handover.

This protects both client and consultant.

26. Proposal

The consultant sends a proposal containing:

- Problem
- Solution
- Scope
- Deliverables
- Timeline
- Pricing
- Payment terms
- Revision policy
- Assumptions
- Exclusions
- Acceptance criteria
- Support period

The project should **not begin merely because the client says "go ahead."**

Written approval is preferable.

27. Development Process

Development follows:

Requirement → Design → Build → Test → Review → Improve

Each major feature is tested before integration into the final system.

28. Quality Assurance

QA checks:

- Functional correctness
- API responses
- Authentication
- Data validation
- AI output format
- Duplicate handling
- Error handling
- Approval logic
- Revision logic
- Publishing
- Database records
- Security

29. Testing Strategy

Positive Testing

Test expected successful workflows.

Negative Testing

Test invalid inputs.

Boundary Testing

Test limits.

Integration Testing

Test APIs together.

Failure Testing

Simulate API failures.

Regression Testing

Ensure revisions do not break existing functionality.

User Acceptance Testing

Client confirms business requirements.

30. Client Demo

The consultant demonstrates:

1. Workflow trigger
2. Trend research
3. AI analysis
4. Content generation
5. WhatsApp approval
6. Modification
7. Revised output
8. Approval
9. Publishing
10. Logging
11. Error handling

The client then provides feedback.

31. Initial Delivery

The first delivery should be clearly labeled:

Version 1.0 — Client Review Build

It is not automatically the final production release.

The client receives a structured review period.

32. Client Feedback

Example client feedback:

"The system works well, but we want the generated captions to sound more conversational and we want the approval message to contain the content hook."

This is a legitimate revision if those elements were part of the original scope or revision allowance.

33. Revision Management

This is one of the most important professional components.

A revision means:

A modification to an already agreed deliverable that remains within the original project scope.

Examples:

- Change wording
- Adjust prompt
- Modify output format
- Change notification text

- Adjust workflow condition

34. Revision vs New Feature

This distinction must be explicit.

Revision

Client says:

"Make the caption shorter."

Original functionality remains the same.

New Feature

Client says:

"Also create a full TikTok automation."

That changes scope.

Therefore:

Revision $\neq$ New Requirement

35. Included Revisions

Example commercial policy:

The project includes two structured revision rounds.

Each revision round may contain consolidated feedback from the client.

36. Revision Round 1

Client requests:

- Shorter captions
- More conversational tone
- Add hook to approval message

These are accepted.

Consultant updates the system.

37. Revision Round 2

Client requests:

- Add brand voice rules
- Change approval wording
- Improve hashtag structure

These are also accepted if within scope.

38. Revision Round 3

Client requests:

"Can you add YouTube Shorts, TikTok, LinkedIn and Facebook publishing too?"

This is not treated as a normal revision.

It becomes a:

Change Request

39. Change Request Process

The consultant responds:

1. Identify requested change.
2. Determine scope impact.
3. Estimate additional work.
4. Provide additional price.
5. Provide revised timeline.
6. Obtain client approval.
7. Implement change.

This prevents uncontrolled scope expansion.

40. Scope Creep

Scope creep occurs when project requirements gradually expand without corresponding changes to:

- Price
- Timeline
- Resources
- Agreement

Example:

Original:

Instagram automation.

Client later requests:

TikTok + YouTube + Facebook + LinkedIn + CRM + mobile application.

That is significant scope expansion.

41. Additional Pricing

Suppose the client requests the additional platforms.

Example:

Change	Additional Price
TikTok	\$200
YouTube	\$200
Facebook	\$150
LinkedIn	\$150
Additional testing	\$100

Additional scope:

\$800

The consultant should not silently absorb the work.

42. Delivery Package

Final delivery includes:

PROJECT/
 ■
 ■■■ Production Workflows
 ■■■ AI Prompts
 ■■■ Database Schema
 ■■■ API Configuration Guide
 ■■■ Environment Variables Guide
 ■■■ User Manual
 ■■■ Technical Documentation
 ■■■ Testing Report
 ■■■ Revision Log
 ■■■ Deployment Guide
 ■■■ Handover Checklist

43. Documentation

Documentation contains:

User Documentation

Explains how the client uses the system.

Technical Documentation

Explains:

- Architecture
- APIs
- Workflow
- Database
- Error handling
- Credentials
- Maintenance

Troubleshooting Documentation

Explains common failures and solutions.

44. Training

A professional handover includes training.

Example:

60-minute training session

Topics:

1. System overview
2. Starting workflow
3. Approval process
4. Revision process
5. Error monitoring
6. Basic maintenance
7. Reporting

45. Client Acceptance

The project is not considered complete simply because files are sent.

Client acceptance should confirm:

- Deliverables received
- Requirements satisfied
- Testing completed
- Known limitations understood
- Documentation received
- Training completed

46. Acceptance Criteria

Example:

"Client acceptance occurs when all Must-Have requirements pass agreed acceptance tests and no Critical or High-severity defects remain unresolved."

This is much stronger than:

"Client says it looks good."

47. Support Period

Example:

14-Day Warranty Support

Includes:

- Bug fixes
- Configuration corrections

- Deployment-related issues

Does not include:

- New features
- New integrations
- Major redesign
- New workflows

Those require a new quotation.

48. Risk Management

Risk	Probability	Impact	Mitigation
API failure	Medium	High	Retry/fallback
AI output error	Medium	Medium	Human approval
Client delay	Medium	Medium	Approval deadlines
Scope creep	High	High	Change control
Credential issue	Medium	High	Early integration
Data loss	Low	High	Backup
Cost increase	Medium	Medium	Usage monitoring

49. Security

Security measures include:

- Secure credential storage
- No API keys inside prompts
- Least-privilege access
- Authentication
- Secret rotation
- Access control
- Logging
- Input validation
- Output validation

50. Backup and Recovery

Critical workflow configurations should be backed up.

Backup strategy:

- Workflow export
- Database backup
- Prompt versioning

- Configuration documentation
- Recovery instructions

51. Performance Management

The consultant monitors:

- Execution time
- API latency
- AI response time
- Error rate
- Workflow success rate
- API usage
- Token consumption

52. Maintenance

After delivery, maintenance can include:

Basic Maintenance

Bug fixes and configuration.

Advanced Maintenance

- New AI models
- New APIs
- New platform integrations
- Optimization
- Analytics
- Security improvements

These can be sold as separate services.

53. Client Satisfaction

Client satisfaction should be measured through:

- Requirement fulfillment
- Reliability
- Usability
- Communication
- Delivery quality
- Responsiveness
- Documentation
- Support

54. Lessons Learned

The project demonstrates several important lessons.

Lesson 1

Never start development from an unclear client statement.

Lesson 2

Requirements must become measurable.

Lesson 3

Scope must be written.

Lesson 4

Pricing must correspond to scope.

Lesson 5

Revisions need boundaries.

Lesson 6

New features require change control.

Lesson 7

Delivery is more than sending files.

Lesson 8

Acceptance criteria protect both parties.

Lesson 9


Documentation is part of the product.


Lesson 10

Professional communication is a technical project skill.

55. Professional Project Lifecycle

The complete lifecycle is:





56. Complete Requirement-to-Delivery Chain

A professional consultant should understand this chain:

Client Problem



Business Requirement



Functional Requirement



Technical Requirement



Scope



Deliverable



Milestone



Acceptance Criteria



Testing



Client Review



Revision



Final Acceptance

This is the fundamental connection between **requirements, delivery and revisions**.

57. Requirements Traceability Matrix

Requirement	Feature	Test	Delivery
FR-01	Automated Trigger	TC-01	V1
FR-02	Trend Research	TC-02	V1
FR-03	AI Analysis	TC-03	V1
FR-04	Approval	TC-04	V1
FR-05	Modification	TC-05	V1
FR-06	Publishing	TC-06	V1
FR-07	Logging	TC-07	V1

This creates **traceability** between what the client requested and what was delivered.

58. Revision Log

Version	Change	Status
V1.0	Initial delivery	Delivered
V1.1	Caption improvements	Completed
V1.2	Approval message update	Completed
V1.3	Brand voice	Completed
V2.0	Additional platforms	Change Request

This prevents confusion about versions.

59. Final Financial Summary

Original Contract

\$1,650

Included Revisions

\$0 additional

Additional Change Requests

\$800

Final Contract Value

\$2,450

This illustrates a key principle:

60. Final Deliverables Checklist

Before closing the project:

Requirements

- Requirements documented
- Scope defined
- Assumptions documented
- Acceptance criteria defined

Development

- Core automation
- AI integration
- API integrations
- Approval workflow
- Revision workflow

QA

- Functional testing
- Integration testing
- Error testing
- Regression testing
- UAT

Delivery

- Production workflow
- Documentation
- Testing report
- User manual
- Training
- Handover

Commercial

- Pricing
- Payment milestones
- Revision policy
- Change request policy
- Support period

Closure

- Client acceptance

- Final version
- Project archive
- Lessons learned
- Maintenance option

61. Final Evaluation

This fake-client simulation demonstrates that professional project delivery is not simply:

"Client asks → freelancer builds → freelancer sends files."

A mature process is:

Problem → Discovery → Requirements → Scope → Estimation → Pricing → Agreement → Planning → Development → QA → Delivery → Feedback → Revision → Acceptance → Handover → Support

The three central topics—**Requirements, Delivery and Revisions**—are therefore interconnected with **scope management, pricing, communication, project management, quality assurance, risk management, change control, documentation, testing and client acceptance**.

The most important professional principle demonstrated by this assignment is:

A successful project is not merely a technically functional product. It is a clearly defined, correctly scoped, properly priced, tested, documented, accepted and supportable solution that solves the client's agreed problem.

Final Formula

Professional Client Project =

Clear Requirements + Controlled Scope + Accurate Pricing + Structured Development + QA + Managed Revisions + Formal Delivery + Client Acceptance + Proper Handover

Assignment Outcome

After completing this simulation, a learner should be able to:

- Extract requirements from vague client requests.
- Convert business needs into technical requirements.
- Define project scope.
- Separate requirements from features.
- Estimate project effort.
- Create professional pricing.
- Establish payment milestones.
- Define deliverables.
- Manage client expectations.
- Distinguish revisions from new requirements.
- Control scope creep.
- Handle change requests.
- Conduct QA and UAT.
- Deliver a professional project.

- Obtain formal acceptance.
- Perform documentation and handover.
- Establish post-delivery support.
- Protect both client and service provider through a structured project-management process.
